

Field Sound Transmission Test Report

Apparent Sound Transmission Class (ASTC)

Report Date:	2024-04-15 00:00:00		
Test Date:	2024-04-04 00:00:00		
DLAA Test No	1.4.1	Source Room:	2nd Floor Bed 1
Test Site	Gentry apts	Receiver Room:	1st Floor Bed 1
Client	Gentry Builders	Test Assembly:	Floor-ceiling

STANDARDS:

ASTM E336-16	Standard Test Method for Measurement of Airborne Sound Attenuation between Rooms in Buildings
ASTM E413-16	Standard Classification for Rating Sound Insulation
ASTM E2235-04(2012)	Standard Test Method for Determination of Decay Rates for Use in Sound Insulation Test Methods

STATEMENT OF CONFORMANCE:

Testing was conducted in accordance with ASTM E336-20, ASTM E413-16, and ASTM E2235-04(2012), with exceptions noted below. All requirements for measuring and reporting Airborne Sound Attenuation between Rooms in Buildings (ATL) and Apparent Sound Transmission Class (ASTC) were met.

TEST ENVIRONMENT:

The source room was 2nd Floor Bed 1. The space was finished, unfurnished. The floor was Carpet. The ceiling was gyp. The walls were gyp. All doors and windows were closed during the testing period. The source room had a volume of approximately 1,176 cu. ft.

The receiver room was 1st Floor Bed 1. The space was finished, unfurnished. The floor was LVT. The ceiling was gyp. The walls were gyp. All doors and windows were closed during the testing period. The source room had a volume of approximately 1,413 cu. ft.

The test assembly measured approximately 12.3x10.6, and had an area of approximately 130.4 sq. ft.

TEST ASSEMBLY:

The tested assembly was the Floor-ceiling. The assembly was not field verified, and was based on information provided by the client and drawings for the project. The client advised that no slab treatment or self-leveling was applied. Results may vary if slab treatment or self-leveling or any adhesive is used in other installations.

Field Sound Transmission Test Report

Apparent Sound Transmission Class (ASTC)

Report Date: 2024-04-15 00:00:00
Test Date: 2024-04-04 00:00:00
DLAA Test No 1.4.1 **Source Room:** 2nd Floor Bed 1
Test Site Gentry apts **Receiver Room:** 1st Floor Bed 1
Client Gentry Builders **Test Assembly:** Floor-ceiling

TEST PROCEDURE:

Determination of space-average sound pressure levels was performed via the manually scanned microphones technique, described in ASTC Test Procedure ASTM E336-16, Paragraph 11.4.3.3. The source room was selected in accordance with ASTM E336-11 Paragraph 9.2.5, which states that 'If a corridor must be used as one of the spaces for measurement of ATL or FTL, it shall be used as the source space.'

Flanking transmission was not evaluated.

To evaluate room absorption, 1 microphone was used to measure 4 decays at 4 locations around the receiving room for a total of 16 measurements, per AIICT Test Procedure ASTM E1007-14

TEST INSTRUMENTATION:

Equipment Type	Manufacturer	Model Number	Serial Number	Last NIST Traceable Calibration	Last Local Calibration
Microphone Pre-Amp	Larson Davis	PRM831	046469	10/24/2022	4/4/2024
Microphone	Larson Davis	377B20	168830	10/20/2022	4/4/2024
Calibrator	Larson Davis	CAL200	5955	10/26/2022	N/A
Amplified Loudspeaker	QSC	K10	GAA530909	N/A	N/A
Noise Generator	NTi Audio	MR-PRO	0162	N/A	N/A
Amplified Loudspeaker	QSC	K10	GAA530909	N/A	N/A
Noise Generator	NTi Audio	MR-PRO	0162	N/A	N/A

Field Sound Transmission Test Report

Apparent Sound Transmission Class (ASTC)

Report Date: 2024-04-15 00:00:00

Test Date: 2024-04-04 00:00:00

DLAA Test No 1.4.1

Source Room: 2nd Floor Bed 1

Test Site Gentry apts

Receiver Room: 1st Floor Bed 1

Client Gentry Builders

Test Assembly: Floor-ceiling

STATEMENT OF TEST RESULTS:

Frequency (Hz)	L1, Average Source Room Level (dB)	L2, Average Corrected Receiver Room Level (dB)	Average Receiver Background Level (dB)	Average RT60 (seconds)	Noise Reduction, NR (dB)	Apparent Transmission Loss, ATL (dB)
125	93.8	71.5	38.6	0.663	22.3	23.3
160	93.2	69.3	34.0	0.573	23.9	24.3
200	88.3	58.2	38.4	0.864	30.1	32.2
250	89.8	55.3	34.2	1.590	34.5	39.3
315	89.6	51.9	25.8	1.169	37.7	41.1
400	89.4	52.4	23.5	1.316	37.0	41.0
500	84.5	46.5	23.8	1.474	38.0	42.5
630	83.6	41.1	21.1	1.338	42.5	46.6
800	85.1	39.0	19.2	1.216	46.1	49.8
1000	83.0	37.3	19.3	1.354	45.7	49.8
1250	83.6	29.9	16.5	1.504	53.7	58.2
1600	81.0	27.1	14.7	1.645	53.9	58.8
2000	79.6	25.2	11.9	1.571	54.4	59.1
2500	82.2	23.7	10.2	1.461	58.5	62.9
3150	83.7	19.7	9.4	1.258	64.0	67.7

ASTC: 45

The Apparent Sound Transmission Class (ASTC) of 45 was calculated. The ASTC rating is based on Apparent Transmission Loss (ATL), and includes the effects of noise flanking. The ASTC reference contour is shown on the next page, and has been fit to the Apparent Transmission Loss values, in accordance with the procedure of ASTC Test Procedure ASTM E336-16

The results stated in this report represent only the specific construction and acoustical conditions present at the time of the test. Measurements performed in accordance with this test method on nominally identical constructions and acoustical conditions may produce different results.

Field Sound Transmission Test Report

Apparent Sound Transmission Class (ASTC)

Report Date:

2024-04-15 00:00:00

Test Date:

2024-04-04 00:00:00

DLAA Test No

1.4.1

Test Site

Gentry apts

Client

Gentry Builders

Source Room:


2nd Floor Bed 1

Receiver Room:

1st Floor Bed 1

Test Assembly:

Floor-ceiling

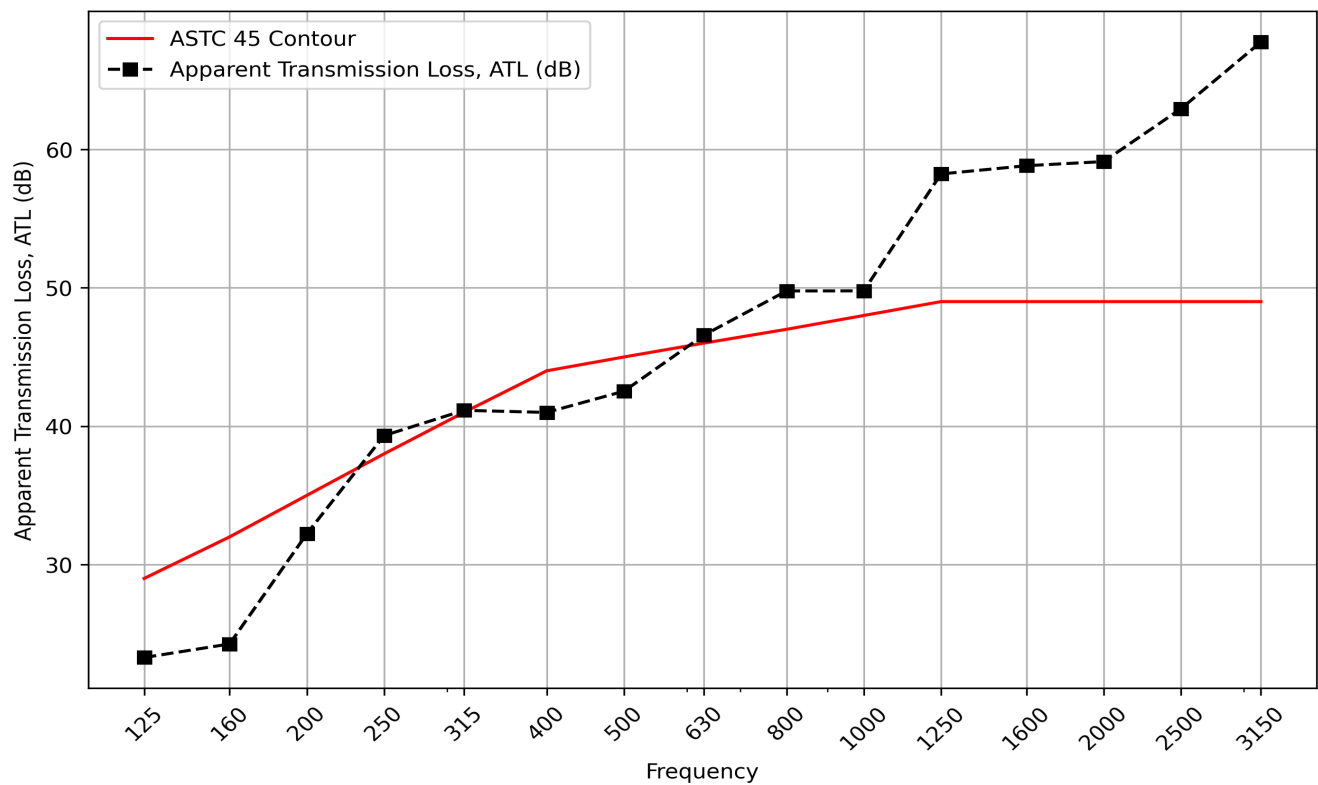

ASTC: 45

test_engineer
test_engineer_signature
test_date
