

# Field Sound Transmission Test Report

## Apparent Sound Transmission Class (ASTC)

**Report Date:** 2024-04-15 00:00:00

**Test Date:** 2024-04-04 00:00:00

**DLAA Test No** 1.1.1

**Test Site** Gentry apts

**Client** Gentry Builders

**Source Room:** 2nd Floor Great Room

**Receiver Room:** 1st Floor Great Room/Kitchen

**Test Assembly:** Floor-ceiling

### STANDARDS:

ASTM E336-20 Standard Test Method for Measurement of Airborne Sound Attenuation between Rooms in Buildings

ASTM E413-16 Standard Classification for Rating Sound Insulation

ASTM E2235-04(2012) Standard Test Method for Determination of Decay Rates for Use in Sound Insulation Test Method

### STATEMENT OF CONFORMANCE:

Testing was conducted in accordance with ASTM E336-20, ASTM E413-16, and ASTM E2235-04(2012), with exceptions noted below. All requirements for measuring and reporting Airborne Sound Attenuation between Rooms in Buildings (ATL) and Apparent Sound Transmission Class (ASTC) were met.

### TEST ENVIRONMENT:

The source room was 2nd Floor Great Room. The space was finished, unfurnished. The floor was Carpet. The ceiling was gyp. The walls were gyp. All doors and windows were closed during the testing period. The source room had a volume of approximately 3,949 cu. ft.

The receiver room was 1st Floor Great Room/Kitchen. The space was finished unfurnished. The floor was LVT. The ceiling was gyp. The walls were gyp. All doors and windows were closed during the testing period. The source room had a volume of approximately 3,949 cu. ft.

The test assembly measured approximately 14.8x29.583, and had an area of approximately 428.0 sq. ft.

### TEST ASSEMBLY:

The tested assembly was the Floor-ceiling. The assembly was not field verified, and was based on information provided by the client and drawings for the project. The client advised that no slab treatment or self-leveling was applied. Results may vary if slab treatment or self-leveling or any adhesive is used in other installations.

# Field Sound Transmission Test Report

## Apparent Sound Transmission Class (ASTC)

**Report Date:** 2024-04-15 00:00:00

**Test Date:** 2024-04-04 00:00:00

**DLAA Test No** 1.1.1

**Test Site** Gentry apts

**Client** Gentry Builders

**Source Room:** 2nd Floor Great Room

**Receiver Room:** 1st Floor Great Room/Kitchen

**Test Assembly:** Floor-ceiling

### TEST PROCEDURE:

Determination of space-average sound pressure levels was performed via the manually scanned microphones technique, described in ASTC Test Procedure ASTM E336-16, Paragraph 11.4.3.3. The source room was selected in accordance with ASTM E336-11 Paragraph 9.2.5, which states that 'If a corridor must be used as one of the spaces for measurement of ATL or FTL, it shall be used as the source space.'

Flanking transmission was not evaluated.

To evaluate room absorption, 1 microphone was used to measure 4 decays at 4 locations around the receiving room for a total of 16 measurements, per ALC Test Procedure ASTM E1007-14

### TEST INSTRUMENTATION:

Sound Level Meter	Larson Davis	831	4328	10/24/2022	4/4/2024
Microphone Pre-Amp	Larson Davis	PRM831	046469	10/24/2022	4/4/2024
Microphone	Larson Davis	377B20	168830	10/20/2022	4/4/2024
Calibrator	Larson Davis	CAL200	5955	10/26/2022	N/A
Amplified Loudspeaker	QSC	K10	GAA530909	N/A	N/A
Noise Generator	NTi Audio	MR-PRO	0162	N/A	N/A
Amplified Loudspeaker	QSC	K10	GAA530909	N/A	N/A
Noise Generator	NTi Audio	MR-PRO	0162	N/A	N/A

construction and acoustical conditions may produce different results.

# Field Sound Transmission Test Report

## Apparent Sound Transmission Class (ASTC)

**Report Date:** 2024-04-15 00:00:00

**Test Date:** 2024-04-04 00:00:00

**DLAA Test No** 1.1.1

**Test Site** Gentry apts

**Client** Gentry Builders

**Source Room:** 2nd Floor Great Room

**Receiver Room:** 1st Floor Great Room/Kitchen

**Test Assembly:** Floor-ceiling

### STATEMENT OF TEST RESULTS:

Frequency (Hz)	L1, Average Source Room Level (dB)	L2, Average Corrected Receiver Room Level (dB)	Average Receiver Background Level (dB)	Average RT60 (seconds)	Noise Reduction, NR (dB)	Apparent Transmission Loss, ATL (dB)
125	95.0	79.5	39.2	0.846	15.5	18.2
160	91.4	73.0	33.0	0.633	18.4	19.9
200	90.0	65.6	37.1	0.996	24.4	27.8
250	91.6	61.6	34.4	1.023	30.0	33.5
315	89.7	57.6	33.7	1.137	32.1	36.1
400	88.8	52.7	33.3	1.345	36.1	40.9
500	84.7	47.5	32.5	1.262	37.2	41.7
630	82.5	42.0	31.2	1.141	40.5	44.5
800	84.5	39.9	30.6	1.118	44.6	48.5
1000	83.0	33.7	29.6	1.287	49.3	53.9
1250	83.8	30.4	28.9	1.459	53.4	58.5
1600	81.4	28.2	28.5	1.518	53.2	58.5
2000	79.8	25.5	24.9	1.461	54.3	59.4
2500	82.4	22.1	20.6	1.393	60.3	65.2
3150	84.0	19.6	18.5	1.403	64.4	69.3

The Apparent Sound Transmission Class (ASTC) of 40 was calculated. The ASTC rating is based on Apparent Transmission Loss (ATL), and includes the effects of noise flanking. The ASTC reference contour is shown on the next page, and has been "fit" to the Apparent Transmission Loss values, in accordance with the procedure of ASTC Test Procedure ASTM E336-16

The results stated in this report represent only the specific construction and acoustical conditions present at the time of the test. Measurements performed in accordance with this test method on nominally identical

# Field Sound Transmission Test Report

## Apparent Sound Transmission Class (ASTC)

Report Date: 2024-04-15 00:00:00

Test Date: 2024-04-04 00:00:00

DLAA Test No

1.1.1

Test Site

Gentry apts


Client

Gentry Builders

Source Room: 2nd Floor Great Room

Receiver Room: 1st Floor Great Room/Kitchen

Test Assembly: Floor-ceiling

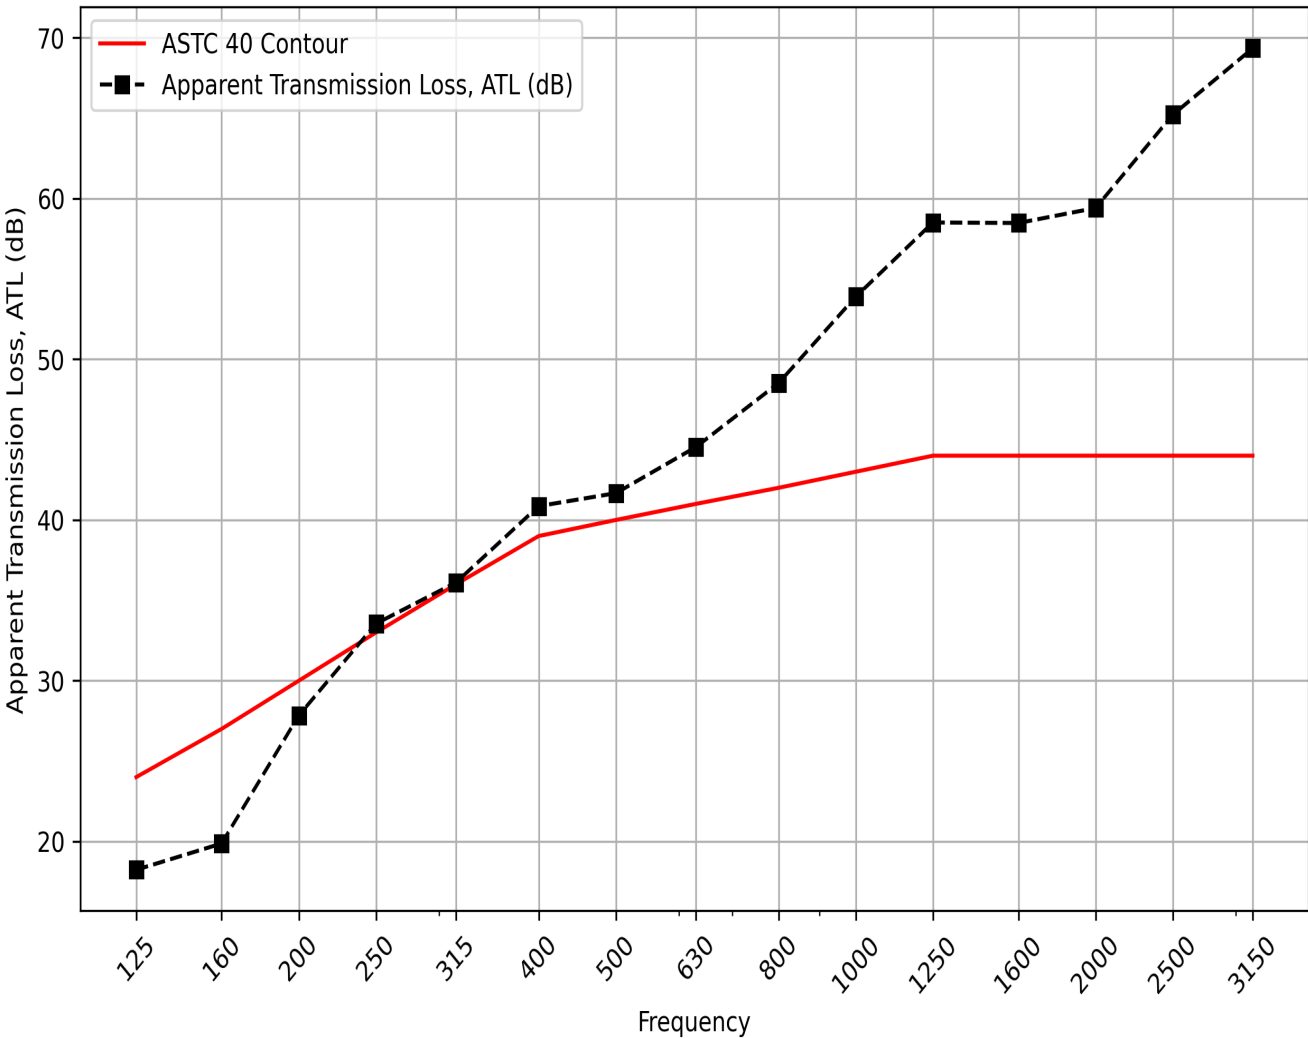

test\_engineer  
test\_engineer\_signature  
test\_date
