

## Field Sound Transmission Test Report

### Apparent Sound Transmission Class (ASTC)

|                     |                  |                       |               |
|---------------------|------------------|-----------------------|---------------|
| <b>Report Date:</b> | 4/9/25           |                       |               |
| <b>Test Date:</b>   | 4/7/25           |                       |               |
| <b>DLAA Test No</b> | 1.3.1            | <b>Source Room:</b>   | Unit 3a       |
| <b>Test Site</b>    | Kaanapali Shores | <b>Receiver Room:</b> | Unit 3b       |
| <b>Client</b>       | Kaanapali AOA    | <b>Test Assembly:</b> | Floor-ceiling |

#### STANDARDS:

|                     |  |
|---------------------|--|
| ASTM E336-16        | Standard Test Method for Measurement of Airborne Sound Attenuation between Rooms in Buildings  |
| ASTM E413-16        | Standard Classification for Rating Sound Insulation  |
| ASTM E2235-04(2012) | Standard Test Method for Determination of Decay Rates for Use in Sound Insulation Test Methods |

#### STATEMENT OF CONFORMANCE:

Testing was conducted in accordance with ASTM E336-20, ASTM E413-16, and ASTM E2235-04(2012), with exceptions noted below. All requirements for measuring and reporting Airborne Sound Attenuation between Rooms in Buildings (ATL) and Apparent Sound Transmission Class (ASTC) were met.

#### TEST ENVIRONMENT:

The source room was Unit 3a. The space was Finished, furnished. The floor was LVT. The ceiling was gyp. The walls were gyp. All doors and windows were closed during the testing period. The source room had a volume of approximately 2867.0 cu. ft.

The receiver room was Unit 3b. The space was Finished, Furnished. The floor was LVT. The ceiling was gyp. The walls were gyp. All doors and windows were closed during the testing period. The source room had a volume of approximately 2867.0 cu. ft.

The test assembly measured approximately 15.25x23.5, and had an area of approximately 358.4 sq. ft.

#### TEST ASSEMBLY:

The tested assembly was the Floor-ceiling. The assembly was not field verified, and was based on information provided by the client and drawings for the project. The client advised that no slab treatment or self-leveling was applied. Results may vary if slab treatment or self-leveling or any adhesive is used in other installations.

## Field Sound Transmission Test Report

### Apparent Sound Transmission Class (ASTC)

**Report Date:** 4/9/25  
**Test Date:** 4/7/25  
**DLAA Test No** 1.3.1  
**Test Site** Kaanapali Shores  
**Client** Kaanapali AOA  
**Source Room:** Unit 3a  
**Receiver Room:** Unit 3b  
**Test Assembly:** Floor-ceiling

#### TEST PROCEDURE:

Determination of space-average sound pressure levels was performed via the manually scanned microphones technique, described in ASTC Test Procedure ASTM E336-16, Paragraph 11.4.3.3. The source room was selected in accordance with ASTM E336-11 Paragraph 9.2.5, which states that 'If a corridor must be used as one of the spaces for measurement of ATL or FTL, it shall be used as the source space.'

Flanking transmission was not evaluated.

To evaluate room absorption, 1 microphone was used to measure 4 decays at 4 locations around the receiving room for a total of 16 measurements, per AIICT Test Procedure ASTM E1007-14

#### TEST INSTRUMENTATION:

| Equipment Type        | Manufacturer | Model Number | Serial Number | Last NIST Traceable Calibration | Last Local Calibration |
|-----------------------|--------------|--------------|---------------|---------------------------------|------------------------|
| Sound Level Meter     | Larson Davis | 831          | 4328          | 10/24/2022                      | 4/4/2024               |
| Microphone Pre-Amp    | Larson Davis | PRM831       | 046469        | 10/24/2022                      | 4/4/2024               |
| Microphone            | Larson Davis | 377B20       | 168830        | 10/20/2022                      | 4/4/2024               |
| Calibrator            | Larson Davis | CAL200       | 5955          | 10/26/2022                      | N/A                    |
| Amplified Loudspeaker | QSC          | K10          | GAA530909     | N/A                             | N/A                    |
| Noise Generator       | NTi Audio    | MR-PRO       | 0162          | N/A                             | N/A                    |

## Field Sound Transmission Test Report

### Apparent Sound Transmission Class (ASTC)

**Report Date:** 4/9/25  
**Test Date:** 4/7/25  
**DLAA Test No** 1.3.1  
**Test Site** Kaanapali Shores  
**Client** Kaanapali AOA  
**Source Room:** Unit 3a  
**Receiver Room:** Unit 3b  
**Test Assembly:** Floor-ceiling

#### STATEMENT OF TEST RESULTS:

| Frequency (Hz) | L1, Average Source Room Level (dB) | L2, Average Corrected Receiver Room Level (dB) | Average Receiver Background Level (dB) | Average RT60 (seconds) | Noise Reduction, NR (dB) | Apparent Transmission Loss, ATL (dB) | Exceptions noted in ASTM E336-16 |
|----------------|------------------------------------|--|--|------------------------|--------------------------|--------------------------------------|----------------------------------|
| 100            | 100.4                              | 61.5   | 34.9                                   | 0.443                  | 39.0                     | 39.5                                 | 0                                |
| 125            | 95.6                               | 55.9   | 36.0                                   | 0.487                  | 39.8                     | 40.7                                 | 0                                |
| 160            | 93.5                               | 55.1   | 34.4                                   | 0.382                  | 38.3                     | 38.2                                 | 0                                |
| 200            | 90.5                               | 53.3   | 33.6                                   | 0.355                  | 37.2                     | 36.7                                 | 0                                |
| 250            | 88.6                               | 51.6   | 33.2                                   | 0.378                  | 37.0                     | 36.9                                 | 0                                |
| 315            | 86.6                               | 48.3   | 33.3                                   | 0.357                  | 38.3                     | 37.9                                 | 0                                |
| 400            | 89.4                               | 43.5   | 32.0                                   | 0.357                  | 45.9                     | 45.5                                 | 0                                |
| 500            | 86.7                               | 32.8   | 30.0                                   | 0.273                  | 53.9                     | 52.3                                 | 1                                |
| 630            | 84.0                               | 28.2   | 29.3                                   | 0.333                  | 55.8                     | 55.1                                 | 1                                |
| 800            | 85.9                               | 27.1   | 26.9                                   | 0.294                  | 58.8                     | 57.5                                 | 1                                |
| 1000           | 85.9                               | 26.6   | 27.5                                   | 0.301                  | 59.4                     | 58.2                                 | 1                                |
| 1250           | 84.3                               | 24.8   | 26.6                                   | 0.345                  | 59.5                     | 58.9                                 | 1                                |
| 1600           | 80.1                               | 21.9   | 24.1                                   | 0.322                  | 58.1                     | 57.3                                 | 1                                |
| 2000           | 77.8                               | 20.9   | 22.4                                   | 0.306                  | 56.9                     | 55.8                                 | 1                                |
| 2500           | 81.2                               | 21.5   | 22.1                                   | 0.314                  | 59.7                     | 58.7                                 | 1                                |
| 3150           | 82.9                               | 21.2   | 21.6                                   | 0.300                  | 61.7                     | 60.5                                 | 1                                |
| 4000           | 83.6                               | 18.4   | 19.5                                   | 0.303                  | 65.1                     | 64.0                                 | 1                                |

**ASTC: 50**

The Apparent Sound Transmission Class (ASTC) of 50 was calculated. The ASTC rating is based on Apparent Transmission Loss (ATL), and includes the effects of noise flanking. The ASTC reference contour is shown on the next page, and has been fit to the Apparent Transmission Loss values, in accordance with the procedure of ASTC Test Procedure ASTM E336-16

The results stated in this report represent only the specific construction and acoustical conditions present at the time of the test. Measurements performed in accordance with this test method on nominally identical constructions and acoustical conditions may produce different results.

## Field Sound Transmission Test Report

### Apparent Sound Transmission Class (ASTC)

Report Date: 4/9/25

Test Date: 4/7/25

DLAA Test No 1.3.1


Test Site Kaanapali Shores

Client Kaanapali AOA

Source Room: Unit 3a

Receiver Room: Unit 3b

Test Assembly: Floor-ceiling

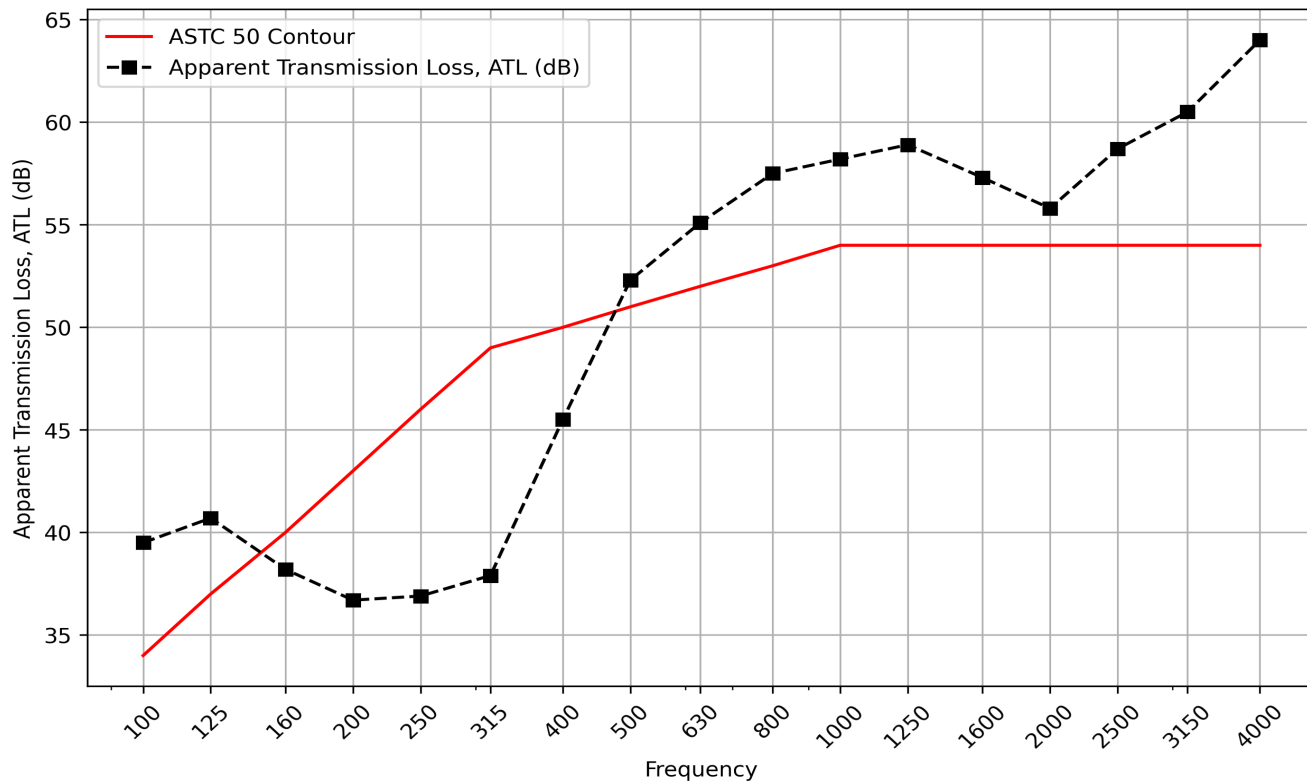

ASTC: 50

Test Conducted By:

Jake Pfitsch, Project Consultant

Zane Wright, Project Consultant
